


Construction Update



Lake County
Division of Transportation
600 West Winchester Road
Libertyville, Illinois 60048



Project Location:

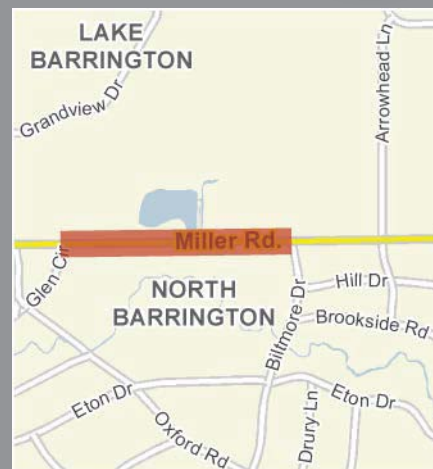

Project:

Miller Rd Improvements

Limits:

Miller Rd from Glen Circle Dr to Biltmore Dr, 0.3 miles east of IL59

Project Description:

This project consists of raising the Miller Rd profile and installing a three-span bridge to alleviate road flooding. Other improvements include road resurfacing, construction of a retaining wall, curb and gutter installation, guardrail, drainage, pavement markings and landscape restoration.

Project Status: **Active**

Project % complete: **50%**

Current Information:

Due to a few days of flooding in the work area & unforeseen circumstances related to the ground conditions, a delay in the opening of the new Miller Rd Bridge will be necessary. Originally when Miller Rd was closed July 22nd, the intention was to reopen on or before October 19th. It will now be reopened to traffic by the evening of Saturday, October 26th.

The posted detour will continue to use IL59 to IL22 to US12. LCDOT coordinated with IDOT so that the resurfacing of IL22 within the detour limits of IL59 to US12 will now be deferred until after October 26 when Miller Rd reopens. IDOT's portion of their resurfacing project west of IL59 to US14 has already been done.

The completion date for the Miller Rd. project is still November 30, 2013. This means that the final surface, landscaping, guardrail, permanent pavement markings and punchlist will be completed under traffic with one lane traffic control using flaggers as necessary during day time hours.

Construction Information Contact:

Jeff Dayson, Resident Engineer
847.381.1547

Additional Contact(s):

Glenn Petko, LCDOT
Engineer of Construction
847.377.7400

Al Giertych, LCDOT
Assistant County Engineer
847.377.7400

Lake County Traffic Information:
lakecountypassage.com

Date: **10/7/13**
