

# Construction Update



Lake County  
Division of Transportation  
600 West Winchester Road  
Libertyville, Illinois 60048



Project:

## Dilleys Rd Resurfacing

Limits:

Dilleys Rd from just south of Wadsworth Rd to Grand Av (IL132).

Project Description:

The project consists of grinding off the riding surface, patching as needed and repaving with two or three new asphalt layers. Related work includes manhole adjustments, bridge deck resurfacing, widened bicycle-friendly asphalt shoulders, aggregate shoulders, spot curb and sidewalk replacement, guardrail, pavement markings, and landscape restoration.

**Project Status: Active**

**Project % complete: 95%**


### Current Information:

All of the surface paving is now complete, final markings are in process then miscellaneous wrap up work like shoulder aggregate and landscaping is to be completed in December.

The damp and cold weather in December did not allow the contractor enough time to finish the bridge waterproofing work this season, so unfortunately it will continue next spring. The east half of the bridge deck south of Wadsworth Rd was paved with temporary asphalt so that the bridge temporary signals could be removed for the winter and both lanes reopened. However, it will be necessary to turn on the one lane signals again next spring for a few days to remove that temporary asphalt, finish the waterproofing and pave the final layer.

This location is part of a three road resurfacing contract that includes Delany (North of Wadsworth Rd to IL173) and Kilbourne (Russell Rd. to WI state line). These other locations have already been completed.

Project Location:

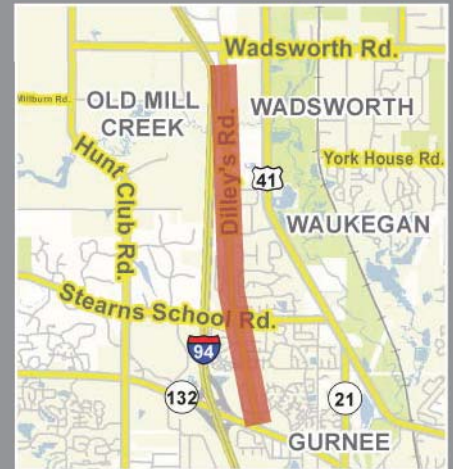

Construction Information Contact:

Matt Mitchell, LCDOT  
Resident Engineer  
Field Office 847.599.7763

Additional Contact(s):

Glenn Petko, LCDOT  
Engineer of Construction  
847.377.7400

Al Giertych, LCDOT  
Assistant County Engineer  
847.377.7400

Lake County Traffic Information:  
[lakecountypassage.com](http://lakecountypassage.com)

Date: 12/6/13
